



User Guide for Critical path Management System



Home Page

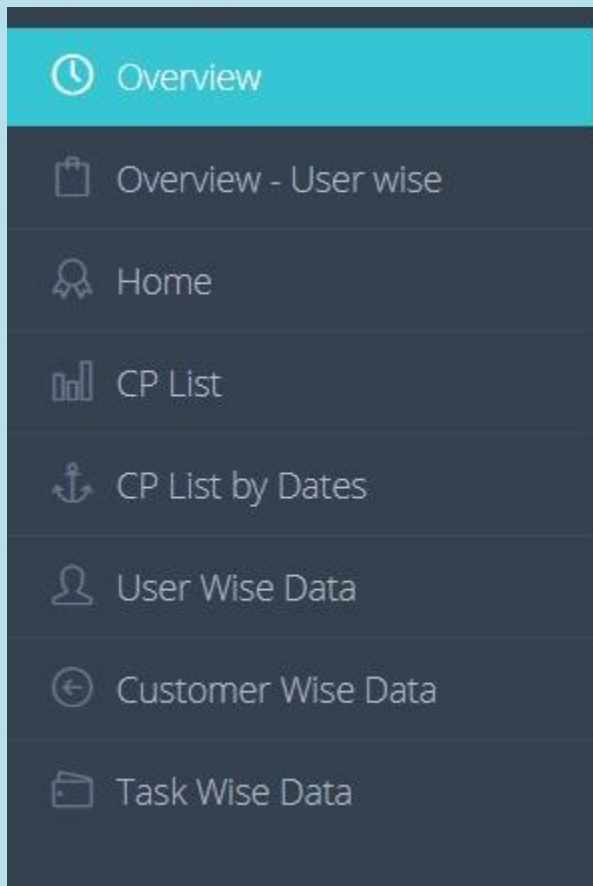

1.Overview

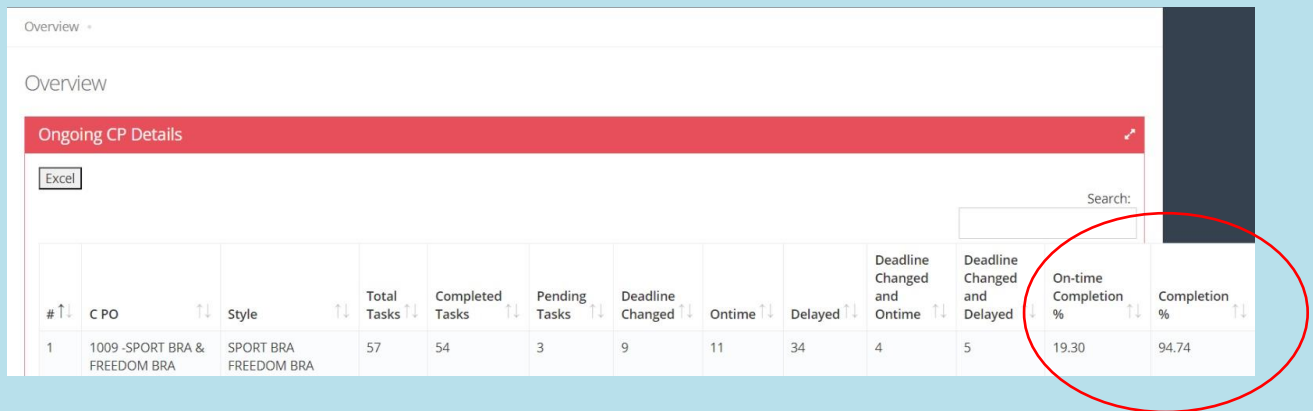

Overview

Overview

Ongoing CP Details

Excel

Search:

# ↑↓	C PO ↑↓	Style ↑↓	Total Tasks ↑↓	Completed Tasks ↑↓	Pending Tasks ↑↓	Deadline Changed ↑↓	On-time ↑↓	Delayed ↑↓	Deadline Changed and On-time ↑↓	Deadline Changed and Delayed ↑↓	On-time Completion % ↑↓	Completion % ↑↓
1	1009 -SPORT BRA & FREEDOM BRA	SPORT BRA FREEDOM BRA	57	54	3	9	11	34	4	5	19.30	94.74

This view shows all the ongoing CP details summary.

Critical path management Metrics

1. **On time completion %** - No of on time completed tasks/ Total tasks X 100 %
2. **Completion %** - No of completed tasks/ total tasks X 100 %

The above two metrics can be viewed for either given CPO or style by using the search button.

2.Overview - User wise

Overview

CP Details

From

To

Action

Load ALL

Load Mine

Excel

Search:

#	C PO	Style	Total Tasks	Completed Tasks	Pending Tasks	Deadline Changed	Ontime	Delayed	Deadline Changed and Ontime	Deadline Changed and Delayed	On-time Completion %	Completion %
No data available in table												

Showing 0 to 0 of 0 entries

Previous

Next

Critical path management Metrics

You can use “Load ALL” to get all the ongoing CPs in the system for a given date range.

You can use “Load Mine” to get all the ongoing CPs under your user login for a given date range.

3 Home

Home

Customer wise CP List

Customer

FREEDOM

Customer PO

PO 1017 (ROSE, CL

Pending

Load

CP Details

Excel

Search:

#	Task	Responsible	Planned Date	Completed Date	User	Comments
1	Packing materials confirmation to Bulk Team	PD	2024-03-20		Surenis	2024-04-04 : SS : POLY BAG PRINT HAS BEEN REJECTED ON 25TH MAR AND 2ND SUBMISSION ON 4TH APRIL AND CUSTOMER AGREED TO APPROVE THE PRINT THROUGH THE IMAGES AND SUPPLIER AGREED TO IN HOUSE THE BULK 10TH APRIL
2	Bulk Ex-mill (TRIMS)	MERCHANDIZING	Prev Date - 2024-04-10 New Date - 2024-06-06		Sandunie	2024-05-17 : SS : NEW DEAD LINE - 2024-06-06 Reason - STRECHLINE DELIVERY 6TH JUN FOR THE ROSE & CLAY 2024-04-04 : SS : ON TRACK

You can view all the pending tasks for a given customer and PO.

Management Tip

Managers can use this to get an update of pending tasks of their pending orders (Eg: for orders with revised ex-fac date due within next week or two)

4 CP List

CP Data

PO wise CP List

PO List - Filter: TF24UWWWRO12439 - TF24UWWWRO12439 Pending Load ALL Load Mine

CP Details

Excel Search:

#	Task	Responsible	Planned Date	Completed Date	User	Comments	Update
1	Packing Artworks submission to customer	MERCHANDISING	2024-07-16		Tharinduj		Comment Complete Update
2	Packing items inhouse	MERCHANDISING	2024-07-26		Tharinduj		Comment Complete Update

Showing 1 to 2 of 2 entries

Previous 1 Next

A user can select his or her **pending tasks** for a **selected PO** and include a comment if required or complete the task.

User can use this to update of pending tasks of a selected PO on the actual task completion date or at least one day prior to weekly CP meeting.

5.CP List by Dates

CP Data

Date range

From

2024-07-01

To

2024-08-15

Filter

Pending

Load

CP Details

Excel

Search:

#	PO	Style	Plant	Task	Responsible	Planned Date	Completed Date	User	Comments	Update
1	TF24UWWWWRO12439	TF24UWWWWRO12439		Packing Artworks submission to customer	MERCHANDISING	2024-07-16		Tharinduj		<div>Comment</div> <div>Complete</div> <div>Update</div>
2	TF24UWWWWRO12439	TF24UWWWWRO12439		Packing Items Inhouse	MERCHANDISING	2024-07-26		Tharinduj		<div>Comment</div> <div>Complete</div> <div>Update</div>

A user can select his or her **pending tasks** for a **given date range** and include a comment if required or complete the task.

This view is recommended for users to update CP tasks as they can get all the pending tasks relevant to user at once for a given date range.

User can use this to update of pending tasks of a given date range on the actual task completion date or at least one day prior to weekly CP meeting.

6. User Wise Data

User wise CP Data

Users

User List

carmelenet@rmholdings.lk

Filter

Pending

Load

From

2024-01-01

To

2024-06-30

Filter

Pending

Load

CP Details

Excel

Search:

# ↑↓	PO ↑↓	Style ↑↓	Plant ↑↓	Task ↑↓	Responsible ↑↓	Planned Date ↑↓	Completed Date ↑↓	User ↑↓	Comments ↑↓
1	PO-0002277 Kylie Girls Organic Cotton Leggings -Lady Bird/Pink Pearl	LM20-LLG-2PKLB/ LM20-LLG-2PKPP	RMI	Fabric + Trim test report	RMH MERCHANT TEAM	Prev Date - 2023-11-27 New Date - 2024-01-12		Carmelenet	2024-01-12 : NY : to be rcvd 12th jan 2024-01-12 : NY : NEW DEAD LINE - 2024-01-12 Reason - date changed
2	WLING/07700 & WLING/07703(N018)	N018	RU SALU	Bulk subs approval (TRIMS)	MERCHANDIZING	2024-01-09		Carmelenet	

You can view tasks of a **selected user** for a given date range by using the filter for All/Completed/Pending tasks.

Management Tip

Managers can use this to get an update of pending tasks for next week or two of his or her team members

7. Customer Wise Data

Customer Wise CP Data

Date range

Customer

×

THIRTEEN AMP-M&Co

×

THIRTEEN AMP ROMAN

×

THIRTEEN AMP SEASALT

From

2024-05-01

To

2024-06-30

Filter

Pending

Load

CP Details

Excel

Search:

#	↑↓	PO	↑↓	Style	↑↓	Plant	↑↓	Task	↑↓	Responsible	↑↓	Planned Date	↑↓	Completed Date	↑↓	User	↑↓	Comments	↑↓
1		TAS1189		TAS1189		RMI		Bulk Fabric inhouse		RMH MERCHANT TEAM		Prev Date - 2024-04-22 New Date - 2024-05-14				Pavithram		2024-05-10 : SM : NEW DEAD LINE - 2024-05-14 Reason - DUE TO VESSEL DELAY CHNAGE THE IN DATE 2024-05-03 : SM :	

You can view tasks of a **selected customer or multiple customers** for a given date range by using the filter for All/Completed/Pending tasks.

Management Tip

Managers can use this to get an update of pending tasks for next week or two of his or her selected customers.

8. Tasks Wise Data

Tasks wise CP Data

Tasks

Customer

AMANTE INDIA

Tasks

Bulk inhouse (fabric) Bulk inhouse (Trims)

Filter

Pending

Load

CP Details

Excel

Search:

#	PO	Style	Plant	Task	Responsible	Planned Date	Completed Date	User	Comments
1	X900776,X900777,T3268 & T3271(BRA05701,BRA05601, PAN05801)	X900776,X900777,T3268 & T3271(BRA05701,BRA05601, PAN05801)	RU SALU	Bulk inhouse (fabric)	MERCHANDIZING	2024-07-18		Sandunie	
2	X900776,X900777,T3268 & T3271 (BRA101601, PAN101701)	X900776,X900777,T3268 & T3271 (BRA101601, PAN101701)	RU SALU	Bulk inhouse (Trims)	MERCHANDIZING	2024-07-18		Carmelenet	

You can view **single task or multiple tasks of a selected customer** by using the filter for All/Completed/Pending tasks
